


# ELEMENTARY SCHOOLS METAL GYM REPLACEMENTS

## 15 SCHOOLS

- ❑ **10 Complete:** **CAMELOT**; CLEAR SPRING; COKER;  
COLONIAL HILLS; **DELLVIEW**;  
HARMONY HILLS; **OAK GROVE**;  
SERNA; WALZEM; WEST AVENUE



- ❑ **5 Under Construction:**

NORTHWOOD

REGENCY PLACE

RIDGEVIEW

WILSHIRE

WINDCREST

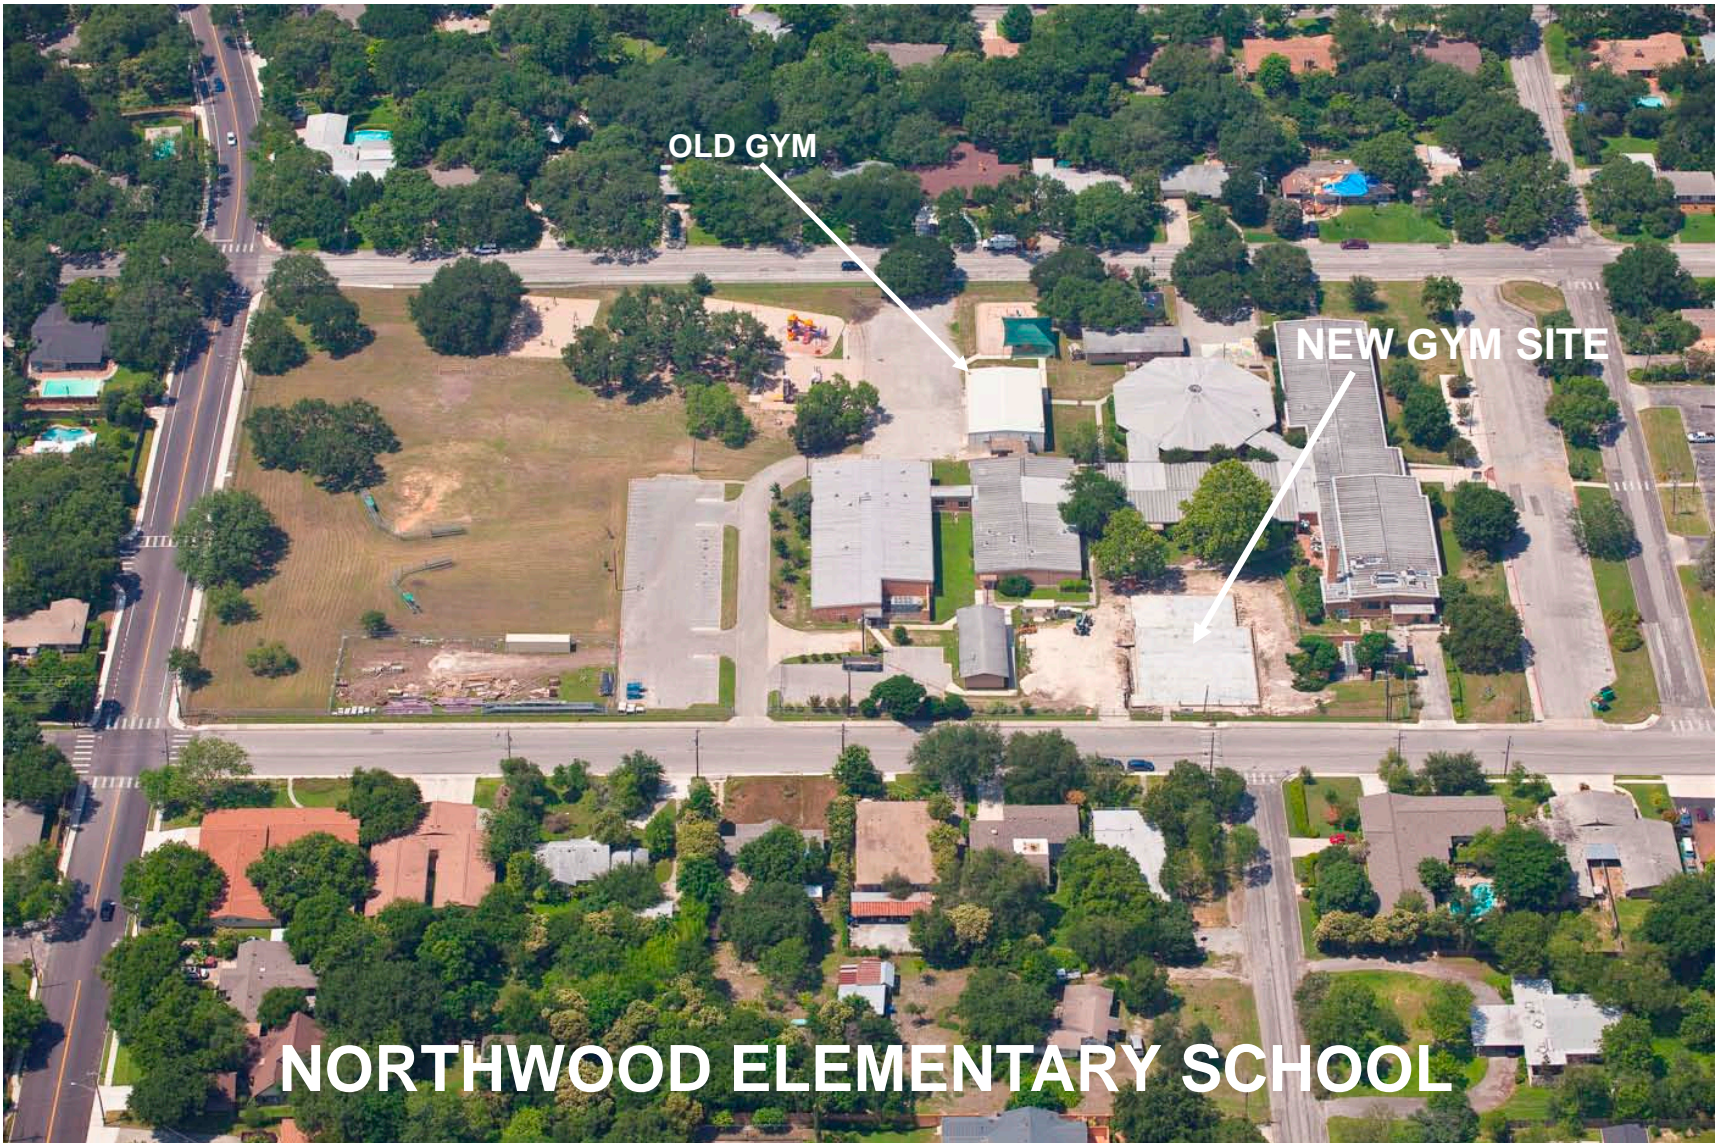


PHOTO DATE: 5 JUN 10



JUN 17 2010



JUN 17 2010



NORTHWOOD ELEMENTARY SCHOOL

JUN 17 2010



JUN 17 2010



# REGENCY PLACE ELEMENTARY SCHOOL

PHOTO DATE: 5 JUN 10

CBAC PRESENTATION, 17 JUN 10

**94% COMPLETE (JUL 10)**



# REGENCY PLACE ELEMENTARY SCHOOL



PHOTO DATE: 5 JUN 10

CBAC PRESENTATION, 17 JUN 10

**61% COMPLETE (AUG 10)**



PHOTO DATE: 5 JUN 10

CBAC PRESENTATION, 17 JUN 10

**37% COMPLETE (OCT 10)**



**NEW GYM**

**OLD GYM**

**WINDCREST ELEMENTARY SCHOOL**

PHOTO DATE: 5 JUN 10

CBAC PRESENTATION, 17 JUN 10

**97% COMPLETE (JUN 10)**
